



Jerry's Girls

Technical Direction

Presentation

By Riley Baheshone



Meet the Team

✦✦ Technical Director: Riley Baheshone ✦✦

Asst. Technical Director: Sean Goebel

Carpenters: Anna Fountain, Sara Hammes, Kenzie
Klatz, Lab Students (20)

** Technical Director Professor: Daniel Staggs

** Shop Supervisor: James Pack

** Shop Carpenter: Michael Meneguín

✦✦ denotes capstone!

** denotes Faculty & Staff

Budget

Budget: \$4000.00

→ Flexibility from past show's budgets.

Current Bid: \$3,913.27

→ Includes AZ Sales Tax & 15%
Contingency.

Collaboration with ATC Scene Shop

- Misc. includes possible charge from use of their shop.

Budget Summary

Bid Name	Bid Sub-Total
Starburst	\$256.52
Pie Platform	\$306.08
Flapjack Platform	\$629.54
Biscuit Platform	\$482.62
Jerry & Geri Platforms	\$326.26
Railing	\$249.00
Stairs	\$475.05
Miscellaneous	\$450.00
Overall Sub-Total	\$3,175.07
Overall Tax (8.25%)	\$261.94
Overall Contingency (15%)	\$476.26
Grand Total	\$3,913.27



Preliminary Build Schedule



1

February 23rd - February 27th

Goal: Platform Construction including lids & facing

- Flapjack, Biscuit, Pie, Jerry, & Geri



2

March 2nd - March 6th

Goal: Continue Platform Construction. Begin Stair Units. Warehouse Trip

- Flapjack, Biscuit, Pie, Jerry, & Geri



**Subject to Change



Preliminary Build Schedule

continued



3

Spring Break!!



4

March 16th - March 20th

Goal: ATC Trip (CNC Starburst) & Continue Stairs.
Start Railing.

- Includes rigging & steel bending.

**Subject to Change





Preliminary Build Schedule

continued



5

March 23rd - March 27th

Goal: Finalize Railing & Sewing Fabric as needed

- Preferably acting more as a float week.



6

Load-in Week...



** Subject to Change

Preliminary Load-in Schedule

Monday March 30th
1:00p-5:00p & 6:00p-10:00p

Platforms in Place
Lid & Face
JC & Sand
Vacuum & Sweep

Tuesday March 31st
1:00p-5:00p & 6:00p-10:00p

Finish Platforms
Attach Railing
Rigging Starburst
Draping Fabric
Sweep



Wednesday April 1st
1:00p-5:00p & 6:00p-10:00p

No monkey business
planned.
Finish Railing
Finish Draping Fabric
Sweep & Mop




 denotes welding in space

 denotes hardhat zone

**Subject to Change

Stock

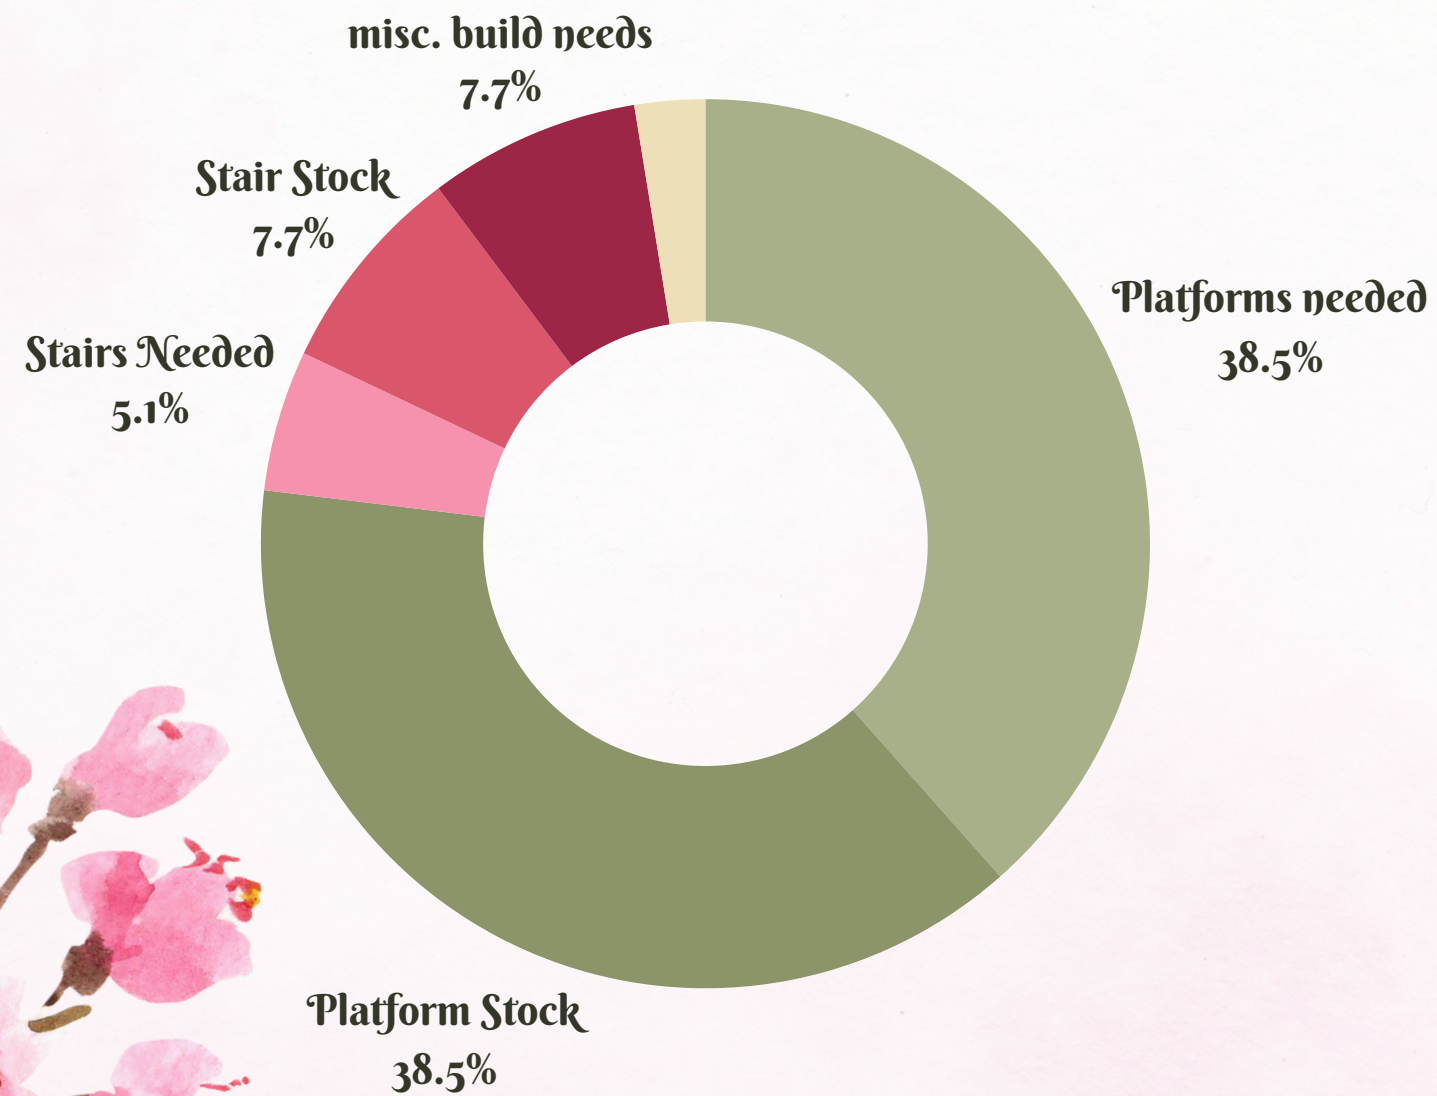


Almost half (1/2) of our projects are already provided through stock.

Yay saving money!




Priority for Paints

- Week 1: Providing Facing & MDF Lids to Paints
 - This includes all the Platforms (Flapjack, Biscuit, Pie, Jerry, & Geri)
 - May spill into second (2nd) week, but no later.
 - Plotting Points Onstage
 - TBD on dates for painting the deck.
 - Load-in Day 1: Routing & Prepping Platforms
 - Goal is to get platforms prepped for paints first.
- 

Questions, Comments, or Concerns?

let me know...





THANK YOU

